


BCC DS
RECEIVED
20/05/2026
APPLICATION REF
A007026963

CONSTRUCTION PROGRAM

240 Queen Street Lobby Upgrade - All Tasks



ID	Text14	Name	Duration	Start	Finish
1		240 QUEEN STREET (5d/w Calendar)	275 days	Wed 21/01/26	Wed 24/02/27
2		TENDER & AWARD	69 days	Wed 21/01/26	Fri 1/05/26
13		CLIENT MATTERS	75 days	Tue 28/04/26	Thu 13/08/26
29		DESIGN PHASE	25 days	Fri 1/05/26	Fri 5/06/26
36		AUTHORITIES	47 days	Fri 1/05/26	Tue 7/07/26
62		KEY MILESTONES	274.5 days	Wed 21/01/26	Wed 24/02/27
84		PRECONSTRUCTION & MOBILISATION - ATG PROJECTS	10 days	Fri 1/05/26	Tue 12/05/26
92		MAIN (CRITICAL) PROCUREMENT ITEMS	189 days	Fri 1/05/26	Mon 7/12/26
167		PRELIMINARIES	206 days	Fri 1/05/26	Wed 24/02/27
174		CONSTRUCTION DURATION	141 days	Fri 26/06/26	Fri 22/01/27
175		SITE ESTABLISHMENT	2 days	Fri 26/06/26	Tue 30/06/26
176		Start Site Establishment	0 days	Fri 26/06/26	Fri 26/06/26
177		Initial Site Set up - location TBC	2 days	Mon 29/06/26	Tue 30/06/26
178		Site Establishment Complete	0 days	Tue 30/06/26	Tue 30/06/26
179		SERVICES & FINISHES	135 days	Tue 30/06/26	Mon 18/01/27
180		Commence finishes & services	0 days	Tue 30/06/26	Tue 30/06/26
181		GENERAL SITE ENABLING WORKS	5 days	Tue 30/06/26	Tue 7/07/26
182		Concrete scanning to enable steel installation under entry stairs	0 days	Tue 30/06/26	Tue 30/06/26
183		Night works	5 days	Wed 1/07/26	Tue 7/07/26
184		Remove existing GF glazed entry door to US of header - weekend works	2 days	Wed 1/07/26	Thu 2/07/26
185		Installation hoarding set-up 1	3 days	Fri 3/07/26	Tue 7/07/26
186		Isolate services as required	5 days	Wed 1/07/26	Tue 7/07/26
187		Site Enabling Works Complete	0 days	Tue 7/07/26	Tue 7/07/26
188		FOYER WORKS	98 days	Wed 8/07/26	Tue 24/11/26
189		Foyer Works - Enclosed workzone	98 days	Wed 8/07/26	Tue 24/11/26
190		Night Works	98 days	Wed 8/07/26	Tue 24/11/26
191		Protection existing lobby tiles	1 day	Wed 8/07/26	Wed 8/07/26
192		Demolition walls, tiles & bulkheads & cladding on grid 3 & existing cafe	14 days	Thu 9/07/26	Tue 28/07/26
193		Framing walls/ceilings & services rough-in's	12 days	Wed 29/07/26	Fri 14/08/26
194		New Entry Auto doors	2 days	Mon 19/10/26	Tue 20/10/26
195		Aluminium cladding above entry doors after cladding	2 days	Wed 21/10/26	Thu 22/10/26
196		Remove hoarding - internal	1 day	Tue 24/11/26	Tue 24/11/26
197		Dayworks	83 days	Wed 29/07/26	Tue 24/11/26
198		Survey as-built structure - incl. report	5 days	Wed 29/07/26	Tue 4/08/26
199		Sheeting & Wall & ceiling cladding (high level)	14 days	Thu 13/08/26	Tue 1/09/26
200		Services fit off - high level areas (incl. feature lights)	5 days	Wed 2/09/26	Tue 8/09/26
201		Final fit off works high level	5 days	Mon 7/09/26	Fri 11/09/26
202		Wall tiling - incl. planters lower level	10 days	Fri 25/09/26	Fri 9/10/26
203		Floor tiling & protection	5 days	Mon 12/10/26	Fri 16/10/26
204		Joinery carcasses & café joinery	12 days	Mon 19/10/26	Tue 3/11/26
205		Waterproofing joinery planters	6 days	Mon 2/11/26	Mon 9/11/26
206		Stone fit off banquet seating	6 days	Mon 2/11/26	Mon 9/11/26
207		Café & joinery fit off - incl. stone	6 days	Wed 4/11/26	Wed 11/11/26
208		General fit off & appliances	6 days	Tue 10/11/26	Tue 17/11/26
209		FF&E	2 days	Mon 16/11/26	Tue 17/11/26
210		Various signage & directory board	4 days	Thu 12/11/26	Tue 17/11/26

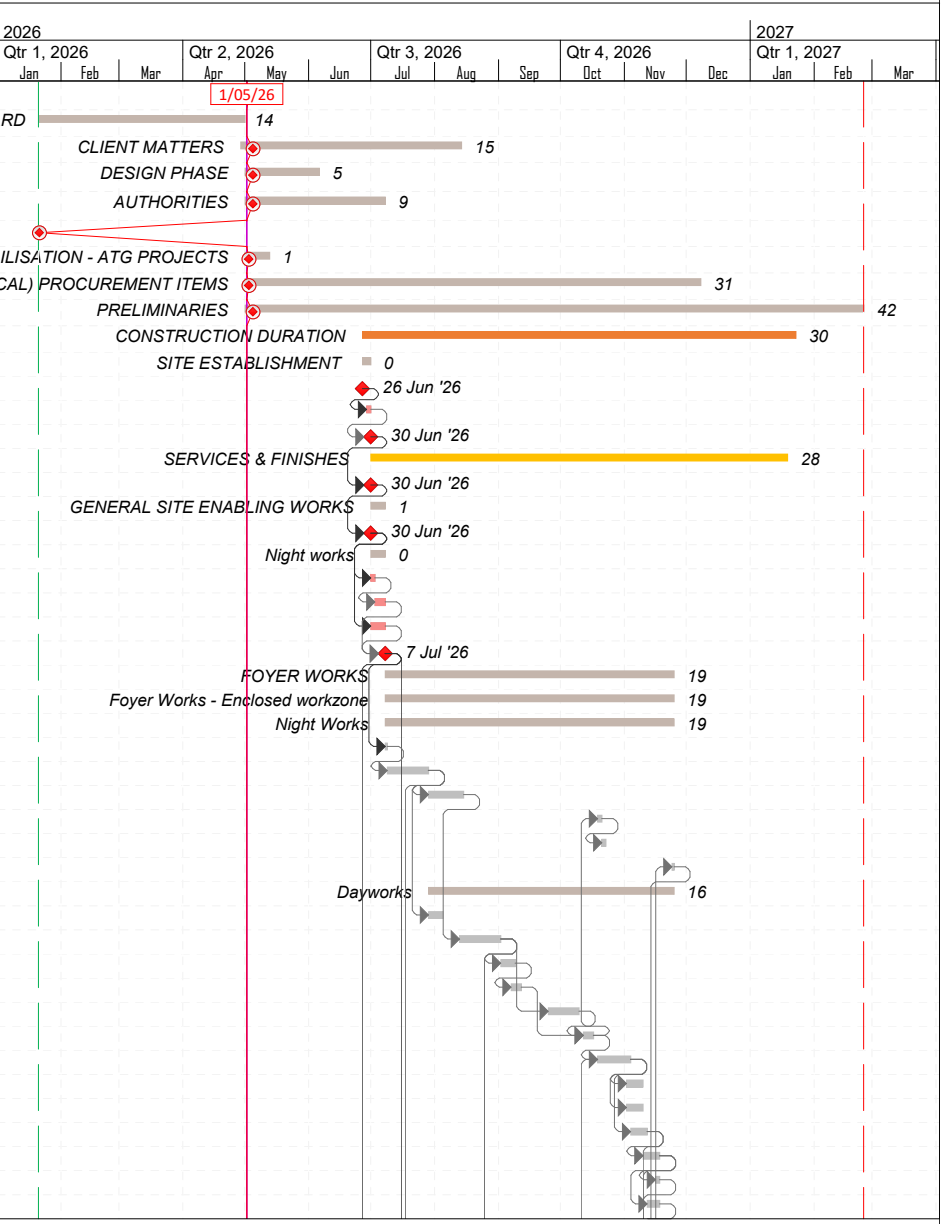

Revision : 240 Queen Street lobby upgrade _rev.0
Print Date: Wed 20/05/26

Baseline	Milestone	◆	Critical Milestone	◆	Baseline Summary	
Baseline Milestone	Summary	—	Client Tasks	—	Progress	—
Tasks	Critical	—	Client Milestones	◆		

